

10/9/2014



JOHN HYLAND  
CONSTRUCTION

## EXECUTIVE SUMMARY REPORT



### **The Past Week**

Completed walls and columns level 9, deck tables moved from level 9 east to level 10. MEP deck rough in underway level 10 east. Mason finishing level 1. Fire sprinkler installation completed level 2 and are running mains on level 3. HVAC ductwork continues level 2. . Exterior framing/dens-glass continues levels 4 and 5. Weather barrier underway east side of the building. Interior framing continues levels 3 and 4. Ceiling framing complete level 2. Plumbing rough in continues levels 2 and 3. Electrical rough in continues level 3. Received and install electrical back-up generator.

### **Coming Next Week**

Place level 10 east deck. Complete level 10 west deck rough in and reinforcement. Weather barrier to start level 2-3. Exterior framing to start level 6 and complete Dens-glass level 5. Weather barrier installation to continue levels 2 and 3. Interior framing complete level 4 continue level 5, layout level 6. Ductwork and fire sprinklers to continue level 3. Electrical rough in to complete 3 begin level 4. Plumbing testing level 2 and continue rough in level 3 and 4.

### **Current Crew Size**

Manpower: 143

<b>Contractor</b>	<b>Scope</b>	<b>Personnel</b>
John Hyland Const.	Vertical Concrete	14
Cascade Tower Crane	Crane Operator	1
CECO	Slab on deck formwork	12
Jet Electrical	Electrical	12
Jet Plumbing	Plumbing	14
Jet Heating	HVAC Duct	4
Jet Fire Prevention	Fire Sprinklers	7
R2M2	Concrete Reinforcement	11
Roberts Surveying	Building Control	2
Western Partitions	Metal Stud Framing	34
Sun Scaffold	Hydraulic Scaffold	2
West Side Iron	Steel Stair Installation	3
Dynasty	Concrete Finishers	10
Hap's Masonry	Interior CMU	9
LJ Pearson	HM Door Frame Install	2
Arctic Sheet Metal	Weather Barrier	6



Entry into parking garage  
CMU complete.



Grouting CMU wall east  
side of level 1 parking  
garage






Electrical back-up generator in place CMU underway to complete the enclosure.



Level 2 tanning bed, sauna and steam room area pre-construction meeting with sauna/steam room installer in progress.



Level 2 kitchen/living room wall backing for casework and TV installed.

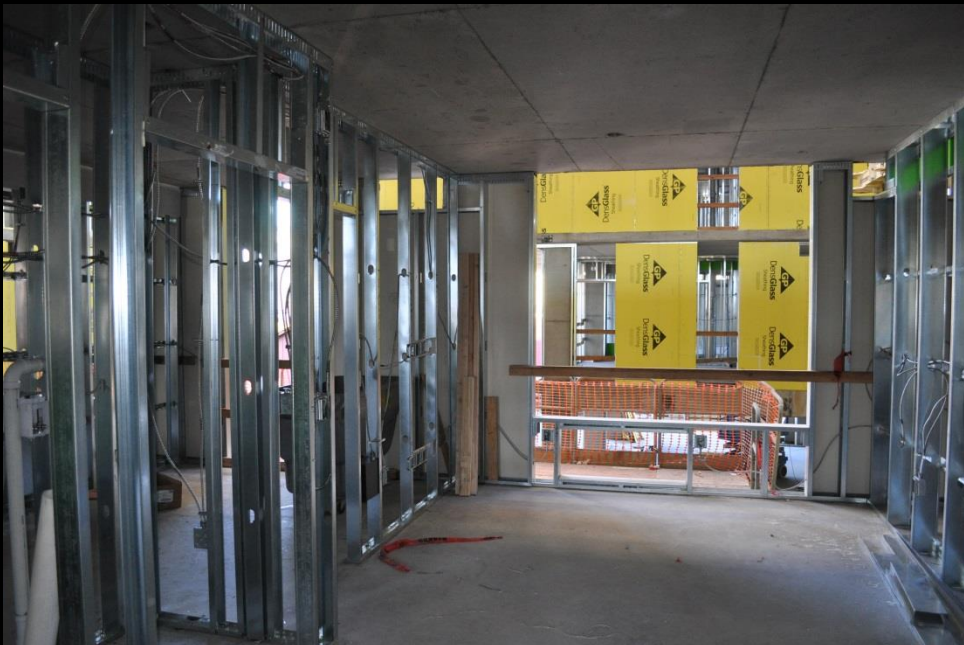


Level 2 looking north from unit entry through room and into courtyard





Level 3 east corridor fire  
pipe installation

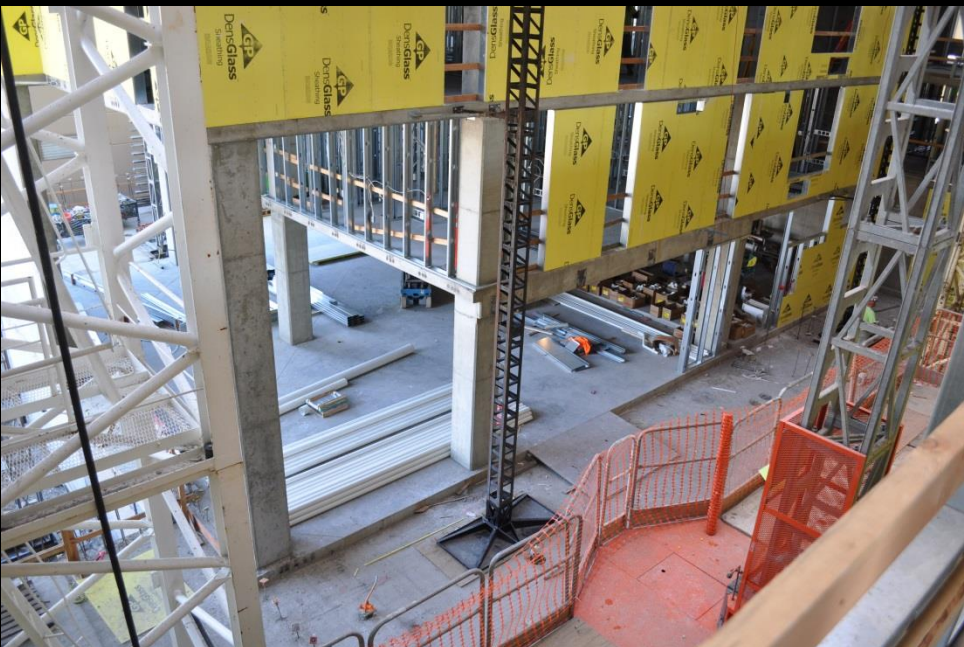

Level 3 south west corner  
of courtyard view from  
unit window to the north  
looking down into  
courtyard and club room.



Exterior level 5 south wall framing.



Level 5 south east corner view to the north interior wall layout in progress.





level 5 north east corner  
view to the south.




Level 4 north wall Dens-  
glass installation





Level 10 east deck MEP  
rough-in in progress

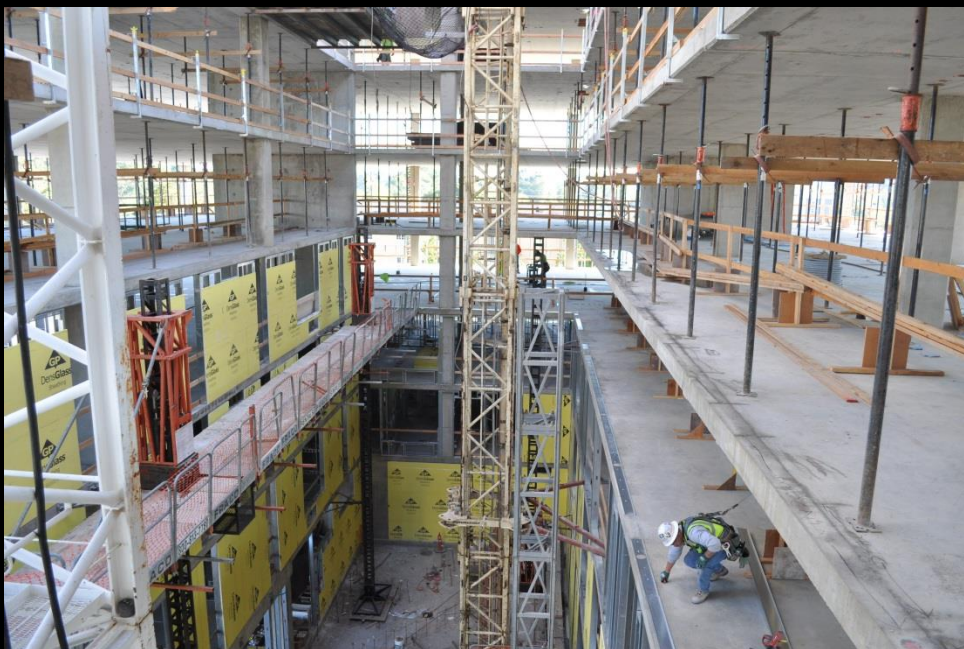

Level 5 west end of  
courtyard view to the east
