




# Happy 4<sup>th</sup> of July!!!

7/2/2015

JOHN HYLAND  
CONSTRUCTION

## EXECUTIVE SUMMARY REPORT

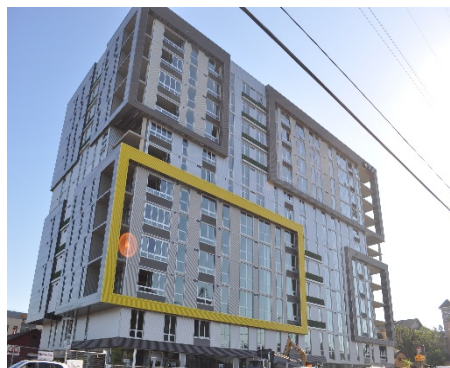

### **The Past Week**

- South side sidewalk forming
- Crosswalk on Broadway
- Drive approach at parking garage
- Exterior window washing
- Tile at rooftop pool and hot tub
- Landscaping at Courtyard
- Casework and countertops at rooms affected by elevator hoist
- Carpet at corridors
- Accessories level 12
- Tile flooring at Leasing Restrooms
- Wood ceiling at Leasing Lobby
- Murphy Bed installation

### **Coming Next Week**

- Corridor carpet continues
- Flooring at rooms affected by elevator hoist
- Accessories level 12 continues
- Wood ceiling in Leasing Lobby continues
- Sidewalk forming and placing continues

### **Current Crew Size**

Manpower: 126

<b>Contractor</b>	<b>Scope</b>	<b>Personnel</b>
John Hyland Const.	Vertical Concrete	8
Jet Electrical	Electrical	14
Jet Plumbing	Plumbing	14
Jet Heating	HVAC Duct	6
Jet Fire Prevention	Fire Sprinklers	2
Western Partitions	Metal Stud Framing/Sheet Rock	4
Third Generation Painting	Interior Paint	10
LJ Pearson	Interior Wood Trim	6
Arctic Sheet Metal	Weather Barrier	1
Dallas Glass	Window Installation	6
Paulsen's	Ceramic Tile	2
Umpqua Roofing	Roof Pavers and Traffic Coating	4
Lanz Cabinets	Casework	2
Thomas Kay	Flooring	6
Rexius	Landscaping and East sidewalk pavers	4
Blake	Countertops	4
ABT Appliances	Appliances	4
Iris	Roller Shades	2
Aqua	Cleaning	5
Knife River	Crosswalk	14
Dynasty Concrete	Water Filtration Planter	6
Anderson Pools	Swimming Pool / Hot Tubs	2



Furnished kitchen area on  
3<sup>rd</sup> floor



Furnished living space on  
3<sup>rd</sup> floor





Furnished bedroom on  
3<sup>rd</sup> floor



Completed Murphy Bed  
installation on 6<sup>th</sup> floor



Corridor carpet and base  
installed on 3<sup>rd</sup> floor



Wood ceiling installation  
at Leasing Lobby



Overall progress at  
Courtyard



Landscaping installed at  
Courtyard





Finishing concrete at  
driveway approach to  
Parking Garage



South sidewalk progress





Crosswalk installed at  
Broadway



Tile installed around  
rooftop hot tub
