


7/31/2015

JOHN HYLAND
CONSTRUCTION

EXECUTIVE SUMMARY REPORT

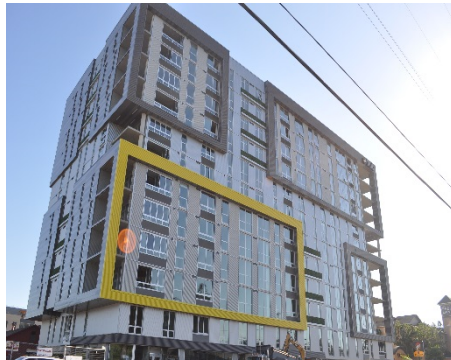

The Past Week

- Exterior window washing
- Turf at Courtyard and North Terrace
- Terrace hot tub install
- Interior signage install
- Misc. hardware on unit entry doors
- Wallcovering in Leasing Lobby and Fitness Area
- Final cleaning
- Owner furniture install
- Testing and balancing
- Final Inspections

Coming Next Week

- Misc. door hardware continues
- Final cleaning continues
- Owner furniture install continues


Current Crew Size

Manpower: 81

Contractor	Scope	Personnel
John Hyland Const.	Vertical Concrete	10
Jet Electrical	Electrical	18
Jet Plumbing	Plumbing	6
Jet Heating	HVAC Duct	4
Jet Fire Prevention	Fire Sprinklers	1
Western Partitions	Metal Stud Framing/Sheet Rock	1
Third Generation Painting	Interior Paint	10
LJ Pearson	Interior Wood Trim	6
Dallas Glass	Window Installation	4
Paulsen's	Ceramic Tile	2
Umpqua Roofing	Roof Pavers and Traffic Coating	4
Lanz Cabinets	Casework	2
Thomas Kay	Flooring	2
Rexius	Landscaping and East sidewalk pavers	2
ABT Appliances	Appliances	2
Aqua	Cleaning	5
Anderson Pools	Swimming Pool / Hot Tubs	2



Wallcovering installed at
Fitness Area

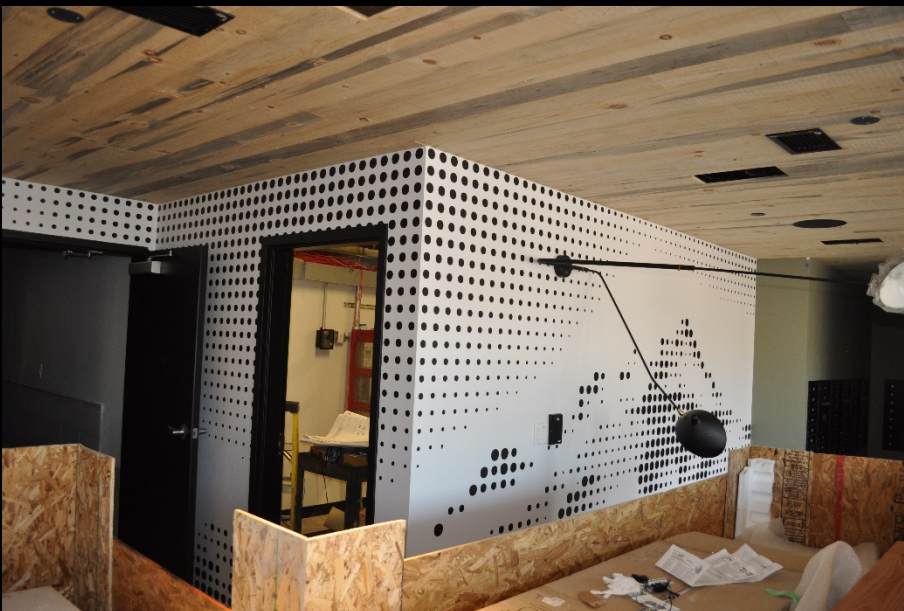

Wallcovering installed at
Leasing Lobby



Pavers and turf complete
on rooftop



Pavers and turf complete
at North Terrace



Furniture installed at level
11 terrace



Hot tub installed at level
11 terrace
